

**ALL GASES SDN. BHD. (963184-D)**

LOT 3778, KAWASAN INDUSTRI MIEL, TELUK KALONG, 24007 KEMAMAN, TERENGGANU

TEL: 09-863 3868


EMAIL: customerservice@allgases.com.my

**MANIFOLD PRESSURE TEST REPORT**

CUSTOMER : B.I.G. INDUSTRIAL GAS SDN BHD REPORT NO. : AGSB/O/21-009  
 ITEM DESCRIPTION : 16 Cylinders Gas Manifold c/w 2 Outlets MANIFOLD ID : B 003  
 TESTING LOCATION : ALL GASES SDN BHD DATE OF TESTING : 21/10/2021

**DETAILS OF EQUIPMENT & TESTING PROCEDURE**

METHOD : HYDROSTATIC TEST  
 DURATION OF HOLDING TEST : 1 MINUTE TYPE OF PRESSURE PUMP : HASKEL M-110-51788  
 TESTING WATER TEMPERATURE : AMBIENT PRESSURE GAUGE S/N NO. : 88Ø1B33L08/19  
 TESTING PRESSURE : 450 BAR (6525 PSI) PRESSURE GAUGE CALIBRATION CERTIFICATE NO. : C/KWM-201829  
 REFERENCE : ASME B31.3 CALIBRATION DUE DATE : 02/11/2021

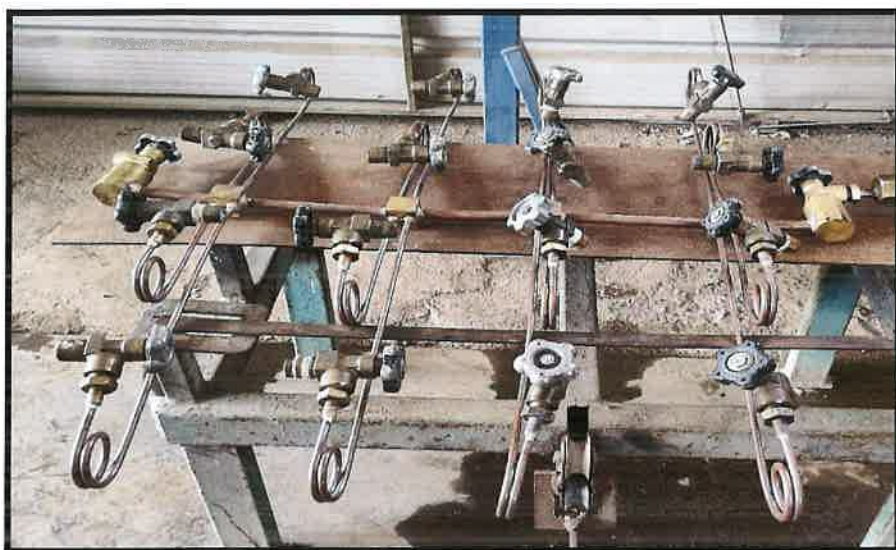

Testing pressure : 450 Bar



Manifold ID : B 003

**TESTING RESULT : PASSED**

**NOTES:** During testing, visual inspection shows no blot or physical changing on copper tubing. Also, no water leakage between copper connection.

TESTED BY :

VERIFIED AND AFFIRMED BY :

WITNESS BY THIRD PARTY

*Shahdi**Mohd*

NAME : MOHD SHAHDI B MD. NOR  
 POSITION : FABRICATION HEAD  
 DATE : 21/10/2021

NAME : MOHD  
 POSITION : SR. ENGINEER  
 DATE : 21/10/2021

NAME : *W. SHAHIDUW*  
 POSITION :  
 DATE : *21/10/2021*

We hereby reported that all the above tests were made accordance with product specification and requirement called of Malaysia Standard & Class Regulations.

Website : [www.allgases.com.my](http://www.allgases.com.my)

Updated Jan. 01, 2020
